

Township of Malahide Sanitary Sewage Collection System

Annual Report

Prepared For: The Corporation of the Township of Malahide

Reporting Period of January 1st – December 31st 2025

Issued: March 13th, 2026

Revision: 0

Operating Authority:



This report has been prepared to meet the requirements set out in:

Document	Document #	Issue Date	Issue Number
CLI-ECA	Number: 051-W601	2023-03-23	1

Table of Contents

- 1 System Description
- 2 Monitoring Data
- 3 Operating Problems and Corrective Actions
- 4 Calibration, Maintenance and Repairs
- 5 Community Complaints and Concerns
- 6 Alterations to the System
- 7 Collection System Overflows and Spills of Sewage

Appendix A - Flow Summary Report

Appendix B - Maintenance Records

1 System Description

The Township of Malahide’s municipal sewage collection system consists of works for the collection and transmission of sewage within the Village of Springfield. Consisting of approximately 6.2km of sewage collection mains ranging in size from 200mm to 250mm, two sewage pumping stations and 3.6 km of forcemain. Sewage is pumped from the Springfield Pumping Station through the 150mm PVC forcemain for 3.6 km to the Ontario Police College Pumping Station (OPC Pump Station). Waste from both the Village of Springfield and the Ontario Police College (OPC) is collected at the OPC pump station (OPC PS). All sewage is then pumped from the OPC pump station and discharge to the Aylmer Lagoons for treatment. The forcemain, which the OPC pump station pumps through, is owned by Infrastructure Ontario. The Springfield and OPC pumping stations are both equipped with back-up power and SCADA monitoring systems.

Springfield Sewage Pumping Station:

The Springfield sewage pumping station is the main pump station for the village of Springfield. The pumping station has a capacity of 1,655 m³/day and is equipped with two sewage pumps (1 duty, 1 standby). The station is connected to a 150 mm diameter forcemain, discharging to the OPC sewage pumping station. The station utilizes SCADA for remote operation, alarm notification and historical trending. There is a 35 kW natural gas standby generator onsite.

Ontario Police College Sewage Pumping Station:

The Ontario Police College Sewage Pumping Station receives sewage from the Springfield sewage pumping station and the Ontario Police College. The pumping station is equipped with two submersible pumps (1 duty, 1 standby), flow meter and associated process piping, valves and controls. The station utilizes SCADA for remote operation, alarm notification and historical trending. There is a diesel standby generator onsite.

2 Monitoring Data

2.1 Springfield Raw Flows

The average daily flow in 2025 was 242.02m³/d, which is down 16.9% compared to the average daily flow in 2024. The average daily flow in 2024 was 291.32m³/d. Refer to Chart 1 for a comparison of the minimum, maximum and average daily flows for 2025. As depicted in Chart 1, flow rates vary in the winter (due to melt) and spring (precipitation) however, during the dryer summer months they are relatively constant. The peak flow in 2025 was 1,201.6m³/d. Chart 2 below shows the monthly average daily flows for 2025 compared against 2024. Refer to Appendix A for a summary of the raw flows.

Chart 1. Springfield minimum, maximum and average daily flow for 2025.


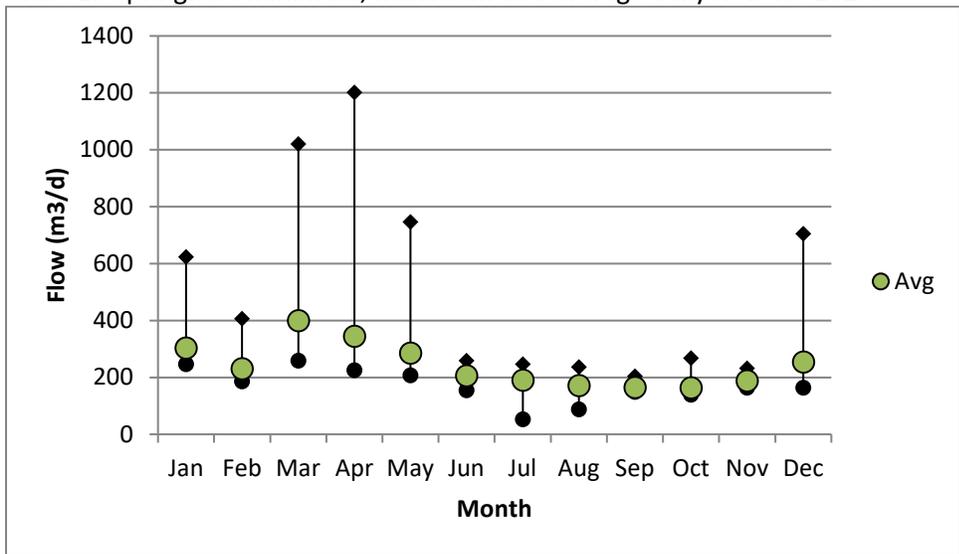


Chart 2. Average monthly flow in 2025 compared to 2024.

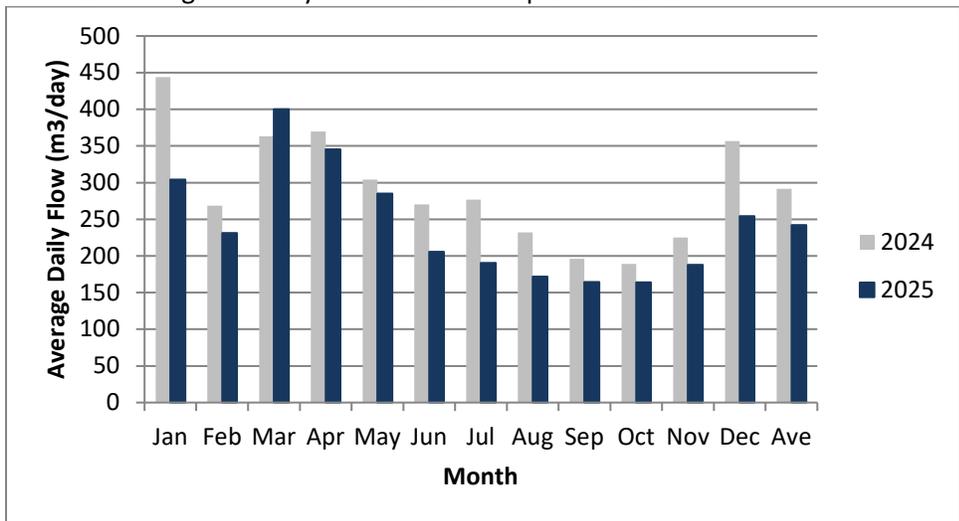

2.2 Ontario Police College Raw Flows

The average daily flow in 2025 for the OPC PS was 497.8m³/day, which is down by 3.4% when compared to the average daily flow in 2024. The average daily flow in 2024 was 515.5 m³/day. Refer to Chart 1 for a comparison of the maximum and average daily flows for 2025. As depicted in Chart 3, flow rates vary in the winter (due to melt) and spring (precipitation) in correlation with flows from Springfield. Flows also fluctuate based on occupancy at the Ontario Police College. The peak flow in 2025 was 461.6m³/d. Chart 4 below shows the monthly average daily flows for 2025 compared against 2024. Refer to Appendix A for a summary of the raw flows.

Chart 3. OPC maximum and average daily flow for 2025.


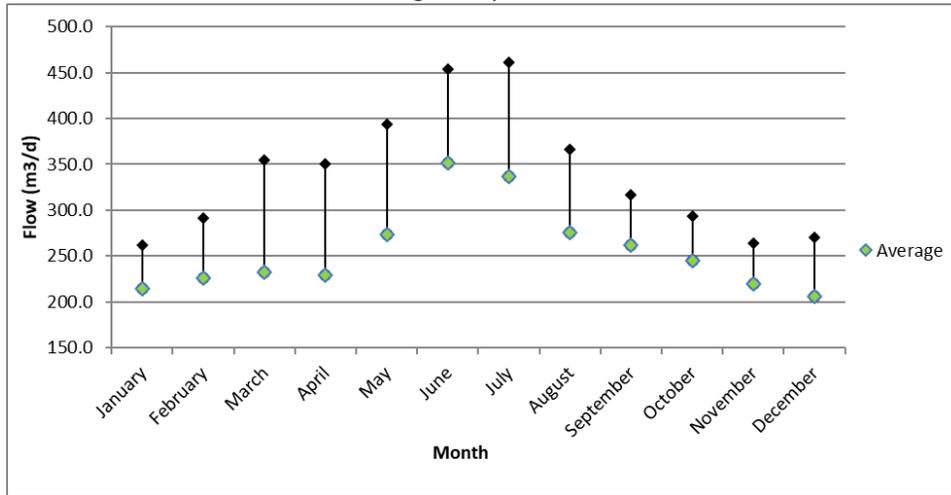


Chart 4. OPC Average monthly flow in 2025 compared to 2024.

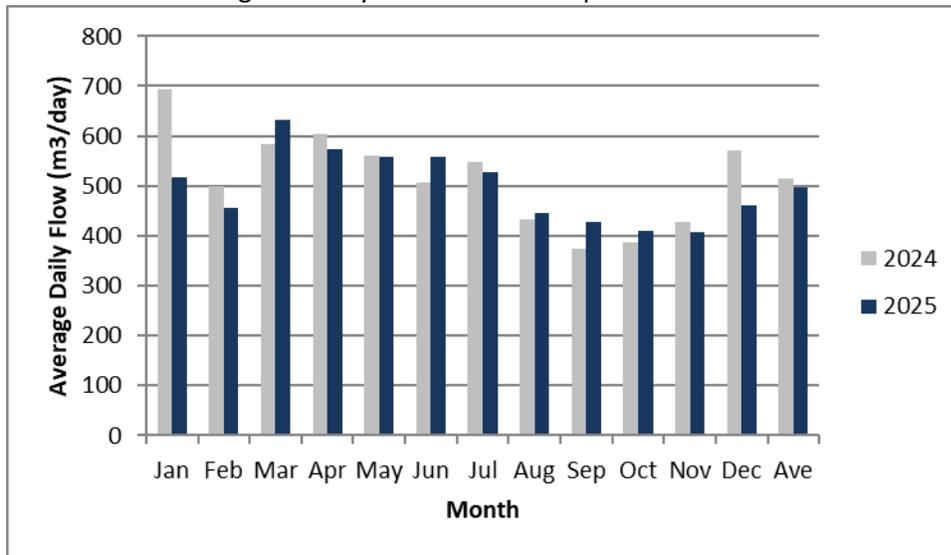

3 Operating Problems and Corrective Actions

Springfield:

No operating problems to report for 2025.

Ontario Police College:

The Ontario Police College pumping station requires frequent cleaning due to oil and grease build-up. On March 27th, July 30th, and December 2nd CC Dance Sewer Cleaning was retained to clean out the wet well.

4 Calibration, Maintenance and Repairs

Regular scheduled preventative maintenance is assigned to the system and monitored using the Workplace Management System (WMS) program. The following is a summary of maintenance performed other than WMS work orders:

- Wet well cleanout and inspections
- Generator maintenance
- Annual WO to assess Drinking Water Threats in the Source Water Protection Area (Requirement of CLI-ECA)
- Installed generator engine coolant overflow reservoir
- Generator wiring upgrade to fix blown fuse during auto transfer
- SCADA routine maintenance
- SCADA server maintenance
- Rain gauge calibration at Springfield PS.
- Springfield flow meter replaced
- Installed pressure gauge transmitter at Springfield
- UPS Inspections
- Flushed and Inspected 2.272km of gravity sewer in Springfield collection system
- Replaced OPC's OIT display

On March 10th and 14th, 2025 SCG Flowmetrix completed the annual calibrations on the flow meters and pressure transmitters at both pumping stations.

Refer to Appendix B for a summary of preventative maintenance work orders.

5 Community Complaints and Concerns

On March 3rd, 11986 Springfield Rd. had a blockage between the service line and collection system. CC Dance was retained to clear the blockage. There were no further issues in 2025.

6 Alterations to the System

There were no alterations completed in the system during the reporting period.

7 Collection System Overflows and Spills of Sewage

There were no overflows or spills that occurred during the reporting period.

Appendix A

Appendix A –Flow Summary

Customized Monthly Report

From 01/01/2025 to 12/31/2025

Facility Name: AYLMER WASTEWATER
TREATMENT LAGOONS
Receiver: Catfish Creek

Facility Org Number: 5536
Facility Owner: Municipality: Town of Aylmer
Service Population:

Works: 110000891
Facility Classification: Class 2 Wastewater Treatment
Total Design Capacity: 6168 m3/day



Raw	Jan 2025	Feb 2025	Mar 2025	Apr 2025	May 2025	Jun 2025	Jul 2025	Aug 2025	Sep 2025	Oct 2025	Nov 2025	Dec 2025
Flow-OPC Flow Meter (OPC and Springfield) - m ³ /d												
IH Edited Count	31.00	28.00	31.00	30.00	31.00	30.00	31.00	31.00	30.00	31.00	30.00	31.00
IH Month.Max	825.10	666.00	1368.70	1551.90	1128.00	659.90	662.50	524.10	505.70	521.70	463.90	888.60
IH Month.Mean	518.40	456.65	631.67	574.11	558.38	556.87	527.27	446.88	426.69	408.80	407.74	460.21
IH Month.Min	428.70	365.60	442.00	412.90	396.10	399.00	383.30	366.70	364.30	338.70	339.00	350.60
IH Month.Total	16070.40	12786.10	19581.80	17223.40	17309.90	16706.00	16345.30	13853.40	12800.70	12672.70	12232.20	14266.50
Flow-Springfield Flow Meter - m ³ /d												
IH Edited Count	31.00	28.00	31.00	30.00	31.00	30.00	31.00	31.00	30.00	31.00	30.00	31.00
IH Month.Max	623.40	406.90	1020.80	1201.60	745.80	259.00	246.80	236.40	203.60	267.70	231.60	705.00
IH Month.Mean	304.04	231.15	399.85	345.28	285.18	205.75	190.57	171.59	164.40	163.96	187.90	254.44
IH Month.Min	246.90	185.60	258.90	225.30	207.70	154.90	52.80	87.90	149.70	139.40	163.60	163.90
IH Month.Total	9425.30	6472.30	12395.50	10358.50	8840.70	6172.40	5907.70	5319.40	4932.10	5082.90	5636.90	7887.60
Flow-OPC Flow (Calculated) - m ³ /d												
IH Edited Count	31.00	28.00	31.00	30.00	31.00	30.00	31.00	31.00	30.00	31.00	30.00	31.00
IH Month.Max	261.60	291.70	354.10	350.30	393.20	453.80	461.60	366.20	316.80	293.00	263.40	270.50
IH Month.Mean	214.36	225.49	231.82	228.83	273.20	351.12	336.70	275.29	262.29	244.83	219.84	205.77
IH Month.Min	152.30	142.60	167.20	159.10	165.80	184.40	192.30	181.30	209.80	194.20	164.10	149.50
IH Month.Total	6645.10	6313.80	7186.30	6864.90	8469.20	10533.60	10437.60	8534.00	7868.60	7589.80	6595.30	6378.90

Customized Monthly Report

From 01/01/2025 to 12/31/2025

Facility Name: AYLMER WASTEWATER
TREATMENT LAGOONS
Receiver: Catfish Creek

Facility Org Number: 5536
Facility Owner: Municipality: Town of Aylmer
Service Population:

Works: 110000891
Facility Classification: Class 2 Wastewater Treatment
Total Design Capacity: 6168 m3/day



		2025			
Raw		Total	Avg	Max	Min
Flow-OPC Flow Meter (OPC and Springfield) - m ³ /d					
	IH Edited Count	365.00			
	IH Month.Max			1551.90	
	IH Month.Mean		498.21		
	IH Month.Min				338.70
	IH Month.Total	181848.40			
Flow-Springfield Flow Meter - m ³ /d					
	IH Edited Count	365.00			
	IH Month.Max			1201.60	
	IH Month.Mean		242.28		
	IH Month.Min				52.80
	IH Month.Total	88431.30			
Flow-OPC Flow (Calculated) - m ³ /d					
	IH Edited Count	365.00			
	IH Month.Max			461.60	
	IH Month.Mean		255.94		
	IH Month.Min				142.60
	IH Month.Total	93417.10			

Appendix B

Appendix B – Maintenance Record

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4299053	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	1/1/25 12:00 AM	1/28/25 08:39 AM	1/28/25 08:39 AM	- Completed
4299215			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	1/1/25 12:00 AM	1/31/25 01:54 PM	1/31/25 01:54 PM	- Completed
4299512			6644, Aylmer Springfield	OPER	Inspection	1	YEARS	Daily O&M Activities Aylmer Springfield WWC (1y) - 6644	COMP	1/1/25 12:00 AM	12/11/25 03:07 PM	12/11/25 07:07 PM	-client connection report -operational rounds and readings
4299743			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	1/1/25 12:00 AM	1/28/25 08:42 AM	1/28/25 08:42 AM	- Completed
4335582			6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	3	MONTHS	Combination Air Valve Insp Plus Springfield PS to OPC forcemain (3m) - 6614	CLOSE	1/14/25 12:00 AM	2/20/25 01:40 PM	2/20/25 01:40 PM	- completed
4352581	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	2/1/25 12:00 AM	2/26/25 03:17 PM	2/26/25 03:17 PM	- Completed monthly generator test
4352746			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	2/1/25 12:00 AM	2/26/25 03:13 PM	2/26/25 03:13 PM	- Completed
4353004			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	2/1/25 12:00 AM	2/21/25 02:26 PM	2/21/25 02:26 PM	- Completed health and safety checks
4353657			6644, Aylmer Springfield	PM	Inspection	3	MONTHS	Wetwell Cleanout Springfield Insp/ Service (3m) - 6644	CLOSE	2/1/25 12:00 AM	6/4/25 09:59 AM	6/4/25 09:59 AM	- completed by CCdans
4361223	0000067863	VALVE GATE 01 EAST PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Annual Gate Valve Inspection/ Exercising (1y) 6644	COMP	2/1/25 12:00 AM	12/9/25 03:59 PM	12/9/25 03:59 PM	-completed valve exercising. Operated smoothly and returned to open position .
4361225	0000067864	VALVE GATE 02 WEST V112 PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Annual Gate Valve Inspection/ Exercising (1y) 6644	COMP	2/1/25 12:00 AM	12/9/25 03:58 PM	12/9/25 03:58 PM	-completed valve gate exercising for pump 1 (west). Valve operated smoothly and was returned to open position

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4361227	0000164827	VALVE CHECK 01 EAST PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Check Valve Annual Inspection/ Servicing (1y/3y) 6644	CLOSE	2/1/25 12:00 AM	10/22/25 03:11 PM	10/22/25 03:11 PM	-completed check valve for pump 1 inspection. Arm raised and fell according to pump running/not running. No abnormal sounds or vibrations, and no sound of backflow or backflow happening according to flow meter either
4361229	0000164828	VALVE CHECK 02 WEST PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Check Valve Annual Inspection/ Servicing (1y/3y) 6644	CLOSE	2/1/25 12:00 AM	10/22/25 03:12 PM	10/22/25 03:12 PM	-completed check valve for pump 2 inspection. Arm raised and fell according to pump running/not running. No abnormal sounds or vibrations, and no sound of backflow or backflow happening according to flow meter either
4365054	0000067869	HEATER ELECTRIC 02 HVAC SYS SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Heater Electric (1y) Inspection 6644	CLOSE	2/1/25 12:00 AM	10/28/25 03:20 PM	10/28/25 03:20 PM	-completed inspection, system free of debris and functions smoothly. watched system run, no abnormal vibration or noise. Inspection passed and successful.
4369350			6644, Aylmer Springfield	PM	Compliance	12	MONTHS	1Y Significant Drinking Water Threats Assessment Review Mallahide	CLOSE	2/1/25 12:00 AM	2/18/25 02:49 PM	2/18/25 02:49 PM	SDWTA review -The significant drining water threats assessment was reviewed. No changes.
4396930	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	3/1/25 12:00 AM	3/13/25 03:26 PM	3/13/25 03:26 PM	- Completed
4397104			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	3/1/25 12:00 AM	3/28/25 02:24 PM	3/28/25 02:24 PM	
4397382			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	3/1/25 12:00 AM	3/13/25 03:26 PM	3/13/25 03:26 PM	- Completed
4397895	0000067866	METER FLOW PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Calibration	1	YEARS	Meter Flow Insp/Service (1y) - 6644	CLOSE	3/1/25 12:00 AM	3/14/25 12:52 PM	3/14/25 12:52 PM	- completed by flow metrix
4401194			6644, Aylmer Springfield	OPER	Inspection	0		6644-WCAY 6644, Aylmer Springfield WWC	CLOSE	3/1/25 12:00 AM	6/6/25 10:10 AM	6/6/25 10:10 AM	

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4409490	0000067847	PANEL TRANSFER AUTOMATIC ATS SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Panel Transfer Service (1y) -6644	COMP	3/1/25 12:00 AM	11/12/25 10:08 AM	11/12/25 10:08 AM	-completed with generator inspection
4409503	0000067849	MCC 01 SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	3	YEARS	Panel Pump Control Center PS Service (3y) - 6644	COMP	3/1/25 12:00 AM	12/18/25 10:33 AM	12/18/25 10:33 AM	- -completed pump control checks, ensuring that pumps pump down at recorded and proper set points. Pumps operate in alternating duty at setpoints set on SCADA. Pump operation as intended and at proper flow rates as well.
4409506	0000067857	LOUVRE MOTORIZED 01 GENERATOR INTAKE SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Louvre Inspection (1y) 5057	CLOSE	3/1/25 12:00 AM	6/6/25 10:18 AM	6/6/25 10:18 AM	- completed by mike
4409508	0000067854	BATTERY CHARGER STANDBY GENSET SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	YEARS	Battery Charger Inspection (1y) 6644	COMP	3/1/25 12:00 AM	12/15/25 03:17 PM	12/15/25 03:17 PM	-completed by gencare during yearly inspection. Battery bank in good condition
4409511	0000334561	UPS BATTERY BANK PLC PANEL SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	YEARS	UPS Battery Bank PLC Panel Inspection (1y) 6644	CLOSE	3/1/25 12:00 AM	10/22/25 03:34 PM	10/22/25 03:34 PM	-completed UPS inspection. In good working order. Batteries are working and supplies power to PLC in the event of an outage, tested during generator transfer. Power to all PLC elements stayed active. Operating temp not too hot, thus fan is working accordingly. All appears normal.
4409518	0000164828	VALVE CHECK 02 WEST PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Valve Check (1y) Inspection 6644	COMP	3/1/25 12:00 AM	11/21/25 03:23 PM	11/21/25 03:23 PM	-completed exercising of valve behind check valve. ensured check valve operated properly and arm went up and down according with flow. No back flow detected .

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4409520	0000164827	VALVE CHECK 01 EAST PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Valve Check (1y) Inspection 6644	COMP	3/1/25 12:00 AM	11/21/25 03:23 PM	11/21/25 03:23 PM	-completed exercising of valve behind check valve of pump 2. ensured check valve operated properly and arm went up and down according with flow. No back flow detected .
4409522	0000067864	VALVE GATE 02 WEST V112 PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Valve Gate (1y) Inspection 6644	CLOSE	3/1/25 12:00 AM	10/28/25 03:23 PM	10/28/25 03:23 PM	-completed isolation valve inspection, exercised valve and ensured valve was left open. Valve operated smoothly and appears in good working order.
4409525	0000067863	VALVE GATE 01 EAST PUMP DISCH SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Valve Gate (1y) Inspection 6644	CLOSE	3/1/25 12:00 AM	10/28/25 03:23 PM	10/28/25 03:23 PM	-completed isolation valve inspection, exercised valve and ensured valve was left open. Valve operated smoothly and appears in good working order.
4445094	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	4/1/25 12:00 AM	4/16/25 03:32 PM	4/16/25 03:32 PM	- completed generator test and filled out required paperwork which has been submitted to return file at Filter Building.
4445245			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	4/1/25 12:00 AM	5/8/25 12:02 PM	5/8/25 12:02 PM	- completed grounds and building maintenance by sweeping and organizing facility.
4445512			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	4/1/25 12:00 AM	5/8/25 11:35 AM	5/8/25 11:35 AM	- completed all signing off on fire extinguisher, eyewash, and first aid kit
4460843	0000334562	PANEL PLC SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	PANEL PLC (1y) - 6644 PLC	CLOSE	4/1/25 12:00 AM	10/22/25 03:31 PM	10/22/25 03:31 PM	-Completed PLC inspection and cleanout. All is in good working order, operating temperature within cabinet is reasonable and in good working order. Light in cabinet in good working order. Vacuumed out cabinet and ensured no wires were taught/ pulling.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4460853	0000067865	VALVE GATE 03 HEADER ISOL SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Valve Gate (1y) Inspection 6644	CLOSE	4/1/25 12:00 AM	10/28/25 03:24 PM	10/28/25 03:24 PM	-completed isolation valve inspection, exercised valve and ensured valve was left open. Valve operated smoothly and appears in good working order.
4460856	0000067868	PUMP SUBMERSIBLE SUMP SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Pump Submers Sump Insp/Service (1y) - 6644	COMP	4/1/25 12:00 AM	12/16/25 03:47 PM	12/16/25 03:47 PM	- Completed pump inspections during wet well clean out. Pumped down well and ensured pump was in good condition. Minimal corrosion and build up. Pumps run good with a steady flow rate. Seals are tight and no abnormal noises on pumps.
4460870	0000334565	SWITCH TEMPERATURE BLDG ALARM SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	YEARS	Transmitter Temperature Service (1y) - 6644	COMP	4/1/25 12:00 AM	12/11/25 12:24 PM	12/11/25 12:24 PM	- Completed temp transmitter inspection all appears normal
4460873	0000067855	LOUVRE MOTORIZED 03 HVAC SYS SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Louvre (1y) Inspection 6644	CLOSE	4/1/25 12:00 AM	9/12/25 03:14 PM	9/12/25 03:14 PM	-watched louvre open and close with temperature change
4487014			6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	3	MONTHS	Combination Air Valve Insp Plus Springfield PS to OPC forcemain (3m) - 6614	CLOSE	4/14/25 12:00 AM	6/3/25 08:31 AM	6/3/25 08:31 AM	- pumped out chambers and inspected for air relief screen on air relief valves, all appears good
4506062	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	5/1/25 12:00 AM	5/29/25 01:50 PM	5/29/25 01:50 PM	- comp 1 hour generator test under load and filled out required paperwork
4506219			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	5/1/25 12:00 AM	5/29/25 01:51 PM	5/29/25 01:51 PM	- completed inside cleaning and organizing as outside is taken care of / in good condition

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4506500			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	5/1/25 12:00 AM	5/29/25 01:53 PM	5/29/25 01:53 PM	- completed OSHA insp and signed off on tags
4507113			6644, Aylmer Springfield	PM	Inspection	3	MONTHS	Wetwell Cleanout Springfield Insp/ Service (3m) - 6644	CLOSE	5/1/25 12:00 AM	6/4/25 03:07 PM	6/4/25 03:07 PM	- completed grating inspection at OPC PS all is flush and does not pose any health and safety risks
4510281			6644, Aylmer Springfield	PM	Compliance	6	MONTHS	FEP Contact List Review Aylmer Springfield (6m) - 6644	CLOSE	5/1/25 12:00 AM	5/14/25 10:58 AM	5/14/25 10:58 AM	FEP Contact List -6644 FEP contact list reviewed. No changes required.
4519269	0000067849	MCC 01 SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Panel Control Pump Service (1y) - 6644	COMP	5/1/25 12:00 AM	11/12/25 10:11 AM	11/12/25 10:11 AM	-panel was inspected in may. and it is in working condition
4543585			6644, Aylmer Springfield	OPER	Inspection	1	YEARS	Grating Insp (1y) - 6644, Aylmer Springfield WWC	CLOSE	5/1/25 12:00 AM	6/4/25 03:09 PM	6/4/25 03:09 PM	- wet well clean out completed in april of 2025
4572503	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	6/1/25 12:00 AM	6/24/25 12:53 PM	6/24/25 12:53 PM	-completed generator test on load and completed required paperwork
4572721			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	6/1/25 12:00 AM	6/24/25 12:55 PM	6/24/25 12:55 PM	-completed building and grounds maintenance
4572998			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	6/1/25 12:00 AM	6/24/25 12:56 PM	6/24/25 12:56 PM	-completed OSHA inspections and signed off on all facility products
4577122			6644, Aylmer Springfield	OPER	Inspection	0		6644-WCAY 6644, Aylmer Springfield WWC	CLOSE	6/1/25 12:00 AM	9/29/25 11:46 AM	9/29/25 11:46 AM	
4593002			6644, Aylmer Springfield	PM	Compliance	1	YEARS	1Y Inspection of Vertical Assets - Springfield Collection System 6644	COMP	6/1/25 12:00 AM	11/21/25 03:26 PM	11/21/25 03:26 PM	-Vertical Asset Inspection Completed during Wet Well Clean out. All materials inside wet well in good condition, no serious corroding. No concerns of instability or poor condition of assets within wet well, in basement (piping), or within facility.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4634501	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	7/2/25 12:00 AM	8/19/25 01:59 PM	8/19/25 01:59 PM	-completed generator test at Springfield and completed required paperwork
4634652			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	7/2/25 12:00 AM	7/16/25 09:13 AM	7/16/25 09:13 AM	-completed building and grounds maintenance for springfield PS
4634912			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	7/2/25 12:00 AM	8/19/25 02:01 PM	8/19/25 02:01 PM	-signed off on fire extinguishers and first aid kit as well as eyewash
4661546			6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	3	MONTHS	Combination Air Valve Insp Plus Springfield PS to OPC forcemain (3m) - 6614	CLOSE	7/14/25 12:00 AM	8/22/25 02:42 PM	8/22/25 02:42 PM	- Co
4678844	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	8/1/25 12:00 AM	8/12/25 02:27 PM	8/12/25 02:27 PM	-completed
4679012			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	8/1/25 12:00 AM	8/12/25 02:28 PM	8/12/25 02:28 PM	-completed
4679281			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	8/1/25 12:00 AM	8/20/25 02:51 PM	8/20/25 02:51 PM	- Co
4679869			6644, Aylmer Springfield	PM	Inspection	3	MONTHS	Wetwell Cleanout Springfield Insp/ Service (3m) - 6644	CLOSE	8/1/25 12:00 AM	8/20/25 02:53 PM	8/20/25 02:53 PM	- Based on quality of wet well clean out not necessary. Client elected to not have wet well cleaned out
4727525	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	9/1/25 12:00 AM	9/13/25 11:55 AM	9/13/25 11:55 AM	-completed
4727702			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	9/1/25 12:00 AM	9/13/25 11:56 AM	9/13/25 11:56 AM	-completed

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4727993			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	9/1/25 12:00 AM	9/13/25 11:57 AM	9/13/25 11:57 AM	-completed
4731465			6644, Aylmer Springfield	OPER	Inspection	0		6644-WCAY 6644, Aylmer Springfield WWC	COMP	9/1/25 12:00 AM	11/27/25 09:00 AM	11/27/25 09:00 AM	
4733142			6644, Aylmer Springfield	OPER	HEALTH AND SAFETY	1	YEARS	OHSA Inspection Aylmer Springfield WWC (1y) - 6644	CLOSE	9/1/25 12:00 AM	9/13/25 11:58 AM	9/13/25 11:58 AM	-completed
4733683	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Engine Natural Gas 01 Standby Insp/ Service (1y) - 6644	CLOSE	9/1/25 12:00 AM	9/13/25 11:56 AM	9/13/25 11:56 AM	-gencare completed inspection August 26
4733708	0000067848	METER LEVEL RAW SEWAGE WET WELL SPRINGFIELD PS CHECK	6644, Aylmer Springfield	PM	Inspection	1	YEARS	Meter Level Insp/Service (1y) - 6644	COMP	9/1/25 12:00 AM	12/16/25 03:50 PM	12/16/25 03:50 PM	- Completed level transmitter inspection. Ensured that reading was accurate and that pump duties operate in accordance with level (duty 1 start at 1.3 stop at 1.00. Duty 2 1.5 stop at 1.1) transducer appears in good condition in wet well. Minimal corrosion and wear.
4779776	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	CLOSE	10/1/25 12:00 AM	10/22/25 03:38 PM	10/22/25 03:38 PM	
4779929			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	CLOSE	10/1/25 12:00 AM	10/22/25 03:40 PM	10/22/25 03:40 PM	-completed building and grounds maintenance. facility cleaned and tidied.
4780203			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	CLOSE	10/1/25 12:00 AM	10/1/25 02:42 PM	10/1/25 02:42 PM	
4780566			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	YEARS	Fire Extinguisher Inspection Aylmer Springfield (1y) - 6644	COMP	10/1/25 12:00 AM	11/5/25 11:10 AM	11/5/25 11:10 AM	-completed

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4786749	0000067850	PUMP SUBMERSIBLE 02 RAW SEWAGE SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Pump Submersible 02 Springfield Ps Insp/Service (1y) - 6644	COMP	10/1/25 12:00 AM	11/27/25 03:22 PM	11/27/25 03:22 PM	-completed inspection of pump 2. Pumped down wet well to get full view of pump. Watched pump operate as instructed. Recorded flow rate during operation. No abnormal noise and flow rate normal and consistent. No leakage detected and all appears in good condition - no excessive rust or wear.
4786758	0000067851	PUMP SUBMERSIBLE 01 RAW SEWAGE SPRINGFIELD PS	6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	1	YEARS	Pump Submersible 01 Springfield Ps Insp/Service (1y) - 6644	COMP	10/1/25 12:00 AM	11/27/25 03:21 PM	11/27/25 03:21 PM	-completed inspection of pump 1. Pumped down wet well to get full view of pump. Watched pump operate as instructed. Recorded flow rate during operation. No abnormal noise and flow rate normal and consistent. No leakage detected and all appears in good condition - no excessive rust or wear.
4816823			6644, Aylmer Springfield	PM	Refurbish/ Replace/Repair	3	MONTHS	Combination Air Valve Insp Plus Springfield PS to OPC forcemain (3m) - 6614	COMP	10/14/25 12:00 AM	12/8/25 05:41 PM	12/14/25 05:43 PM	- Completed in October 2025
4833251	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	COMP	11/1/25 12:00 AM	11/12/25 03:40 PM	11/12/25 03:40 PM	-Completed generator test and completed proper paperwork. Alarm received and acknowledged and utility power transferred back seamlessly.
4833386			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	COMP	11/1/25 12:00 AM	11/12/25 03:41 PM	11/12/25 03:41 PM	-completed cleaning of facility. Grounds work completed by third party. Garbage taken out and floors swept and facility dusted.
4833655			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	COMP	11/1/25 12:00 AM	11/27/25 03:18 PM	11/27/25 03:18 PM	-Completed OSHA inspection and signed off on all OSHA materials. All up to date and accessible for use.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4834291			6644, Aylmer Springfield	PM	Inspection	3	MONTHS	Wetwell Cleanout Springfield Insp/ Service (3m) - 6644	COMP	11/1/25 12:00 AM	12/2/25 02:24 PM	12/2/25 02:24 PM	-completed Springfield Wet Well cleanout. Wet well pumped down and cleaned thoroughly. All appears normal and in good working order.
4836757			6644, Aylmer Springfield	PM	Compliance	6	MONTHS	FEP Contact List Review Aylmer Springfield (6m) - 6644	COMP	11/1/25 12:00 AM	11/6/25 10:55 AM	11/6/25 10:55 AM	FEP Contact List -Springfield's FEP contact list is up-to-date.
4838203			6644, Aylmer Springfield	PM	Compliance	1	YEARS	FEP Review Aylmer Springfield (1y) - 6644	COMP	11/1/25 12:00 AM	12/10/25 08:09 AM	12/10/25 08:09 AM	FEP Review -Springfield's FEP reviewed.
4838493			6644, Aylmer Springfield	PM	Compliance	2	YEARS	FEP Site Plan Review Aylmer Springfield (2y) - 6644	COMP	11/1/25 12:00 AM	12/10/25 08:42 AM	12/10/25 08:42 AM	FEP Site Plan Review -Springfield's FEP site plan reviewed.
4878858	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	COMP	12/1/25 12:00 AM	12/9/25 03:56 PM	12/9/25 03:56 PM	-completed generator run for month of December. Transfer successful and all appears normal
4879172			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	BUSCOMP	12/1/25 12:00 AM	12/15/25 03:14 PM	12/15/25 03:14 PM	-completed building and grounds maintenance by cleaning up facility and sweeping and dusting.
4879455			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer Springfield (1m) - 6644	COMP	12/1/25 12:00 AM	12/2/25 02:35 PM	12/2/25 02:35 PM	-completed OSHA material sign off. All items up to date and unexpired including first aid kit, portable eye wash, and fire extinguisher.
4928502	0000067852	ENGINE NATURAL GAS STANDBY GEN SPRINGFIELD PS	6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Engine Natural Gas Test/Insp (1m) - 6644	COMP	1/1/26 12:00 AM	1/6/26 03:36 PM	1/6/26 03:36 PM	- Completed generator run test successfully. Transfer successful and ran on load. Alarms ack
4928642			6644, Aylmer Springfield	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6644	COMP	1/1/26 12:00 AM	1/6/26 03:38 PM	1/6/26 03:38 PM	- Completed building maintenance by vacuuming and sweeping and wiping surfaces down

Workorder Summary Report

Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6644,6644-WCAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4929174			6644, Aylmer Springfield	PM	HEALTH AND SAFETY	1	MONTHS	OSHA Inspection Aylmer Springfield (1m) - 6644	COMP	1/1/26 12:00 AM	1/6/26 03:37 PM	1/6/26 03:37 PM	- Completed OSHA inspection and sign off onsite including first aid and fire ext

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4299507			6643, Aylmer OPC Pump	OPER	Inspection	1	YEARS	Daily O&M Activities Aylmer OPC Pumping Stn (1y) - 6643	COMP	1/1/25 12:00 AM	1/5/26 11:03 AM	1/5/26 11:03 AM	-client connection report -operational rounds and readings
4299732	0000164914	LIGHTING EMERGENCY 01 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	1/1/25 12:00 AM	1/28/25 08:27 AM	1/28/25 08:27 AM	- Completed
4315307	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	1/1/25 12:00 AM	1/28/25 08:28 AM	1/28/25 08:28 AM	- Completed
4318706			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	1/1/25 12:00 AM	1/31/25 01:50 PM	1/31/25 01:50 PM	- Completed January 16
4334444			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	1/9/25 12:00 AM	1/31/25 01:51 PM	1/31/25 01:51 PM	- Completed
4352993	0000164914	LIGHTING EMERGENCY 01 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	2/1/25 12:00 AM	2/26/25 03:40 PM	2/26/25 03:40 PM	- Completed monthly health and safety inspection
4361561	0000063419	VALVE GATE 01 CHAMBER 03 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	OPC Chamber #3 Annual 6" Gate Valve Inspection/Exercising (1y) 6644	COMP	2/1/25 12:00 AM	12/17/25 03:37 PM	12/17/25 03:37 PM	-gate valve not exercised as per WWOM
4361563	0000063421	VALVE GATE 02 CHAMBER 03 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	OPC Chamber #3 Annual 3" Gate Valve Inspection/Exercising (1y) 6644	COMP	2/1/25 12:00 AM	12/17/25 03:37 PM	12/17/25 03:37 PM	-gate valve not exercised as per WWOM
4364432	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	2/1/25 12:00 AM	2/20/25 03:31 PM	2/20/25 03:31 PM	- Completed monthly generator testing
4366258	0000063418	VALVE AIR RELEASE 02 CHAMBER 03 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	OPC Chamber #3 Annual Air Relief Valve Inspection/Service (1y) 6644	COMP	2/1/25 12:00 AM	12/17/25 03:35 PM	12/17/25 03:35 PM	-air valve inspections completed and documented properly as per monthly inspection
4366667			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	2/1/25 12:00 AM	2/21/25 03:00 PM	2/21/25 03:00 PM	
4379202			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	2/9/25 12:00 AM	2/21/25 02:59 PM	2/21/25 02:59 PM	

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4397371	0000164914	LIGHTING EMERGENCY 01 AYLME R OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	3/1/25 12:00 AM	3/21/25 12:35 PM	3/21/25 12:35 PM	- completed
4401192			6643, Aylmer OPC Pump	OPER	Inspection	0		6643-SPAY 6643, Aylmer OPC Pumping Stn	CLOSE	3/1/25 12:00 AM	6/6/25 10:10 AM	6/6/25 10:10 AM	
4408815	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	3/1/25 12:00 AM	3/28/25 02:34 PM	3/28/25 02:34 PM	
4408834	0000164894	METER FLOW RAW SEWAGE AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Calibration	1	YEARS	Transmitter Flow (1y) Service 6643	CLOSE	3/1/25 12:00 AM	3/28/25 02:30 PM	3/28/25 02:30 PM	- completed
4411211			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	3/1/25 12:00 AM	3/28/25 02:32 PM	3/28/25 02:32 PM	- completed
4425175			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	3/9/25 12:00 AM	3/21/25 12:33 PM	3/21/25 12:33 PM	- completed
4445501	0000164914	LIGHTING EMERGENCY 01 AYLME R OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	4/1/25 12:00 AM	5/8/25 12:04 PM	5/8/25 12:04 PM	- completed signing off on first aid kit, fire extinguisher and eyewash
4460110	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	4/1/25 12:00 AM	7/4/25 08:41 AM	7/4/25 08:41 AM	-completed generator run for 1 hour in the month of april. All ran accordingly
4460129	0000164884	SWITCH TRANSFER AUTOMATIC ATS STANDBY GEN AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	Transfer Switch Service (1y) - 6643	COMP	4/1/25 12:00 AM	11/12/25 10:05 AM	11/12/25 10:05 AM	-completed with generator inspection
4460140	0000164896	LIFTING DEVICE DAVIT ARM 01 AYLME R OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	YEARS	Lifting Equipment Insp (1y) 6643	CLOSE	4/1/25 12:00 AM	6/6/25 10:12 AM	6/6/25 10:12 AM	- Completed by hamisco
4460143	0000164895	METER LEVEL WET WELL AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Calibration	1	YEARS	Transmitter Level 2 Service (1y) - 6643	COMP	4/1/25 12:00 AM	12/16/25 03:56 PM	12/16/25 03:56 PM	- Level transmitter inspection complete. Transducer in good condition with minimal wear/corrosion. Accuracy tested and measured. Equipment in good condition.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4460148	0000164893	TRANSMITTER TEMP AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Transmitter Temperature Service (1y) - 6643	COMP	4/1/25 12:00 AM	11/12/25 10:09 AM	11/12/25 10:09 AM	-completed in April. in working condition
4460615	0000334553	PUMP SUBMERSIBLE SUMP AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	Pump Submers Sump Insp/Service (1y) - 6644	COMP	4/1/25 12:00 AM	11/24/25 03:39 PM	11/24/25 03:39 PM	-sump pump inspection complete. All in good working order, chamber dry. Oil replaced in pump this year by Koolen Electric and Client
4460625	0000164918	FAN EXHAUST WET WELL VENT AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	Exhaust Fan Insp/Service (1y) - 6643	COMP	4/1/25 12:00 AM	12/9/25 03:54 PM	12/9/25 03:54 PM	-completed vent inspection. All inner workings are operating with no obstructions. Cleaned grease from screen and ensured no abnormal noises.
4463339			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	4/1/25 12:00 AM	7/4/25 08:43 AM	7/4/25 08:43 AM	-completed high level and power failure test for the month of april. Alarm recieved and acknowledged.
4486297			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	4/9/25 12:00 AM	6/4/25 09:47 AM	6/4/25 09:47 AM	- completed
4506489	0000164914	LIGHTING EMERGENCY 01 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	5/1/25 12:00 AM	7/4/25 08:45 AM	7/4/25 08:45 AM	-completed OSHA insp and sign offs onsite
4518587	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	5/1/25 12:00 AM	7/4/25 08:46 AM	7/4/25 08:46 AM	-generator test ran 1 hour and completed proper paperwork for the month of may
4519054	0000164907	PUMP SUBMERSIBLE 01 RAW SEWAGE AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	PUMP SUBMERSIBLE RAW 01 ANNUAL (1yr) 6643	COMP	5/1/25 12:00 AM	12/17/25 08:29 AM	12/17/25 08:29 AM	-completed pump inspection during clean out. pump has minimal corrosion and is in good condition. Power sprayed pump to wash off debris. Plug seals in good condition and pump operates effectively.
4519057	0000164908	PUMP SUBMERSIBLE 02 RAW SEWAGE AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	PUMP SUBMERSIBLE RAW 02 ANNUAL (1yr) 6643	COMP	5/1/25 12:00 AM	12/17/25 08:29 AM	12/17/25 08:29 AM	-completed pump inspection during clean out. pump has minimal corrosion and is in good condition. Power sprayed pump to wash off debris. Plug seals in good condition and pump operates effectively

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4521261			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	5/1/25 12:00 AM	7/4/25 08:48 AM	7/4/25 08:48 AM	-completed alarm testing for may, high level and power failure
4543573			6643, Aylmer OPC Pump	OPER	Inspection	1	YEARS	Grating Insp (1y) - 6643, Aylmer OPC Pumping Stn	CLOSE	5/1/25 12:00 AM	9/12/25 03:01 PM	9/12/25 03:01 PM	-completed
4552464			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	5/9/25 12:00 AM	6/4/25 09:52 AM	6/4/25 09:52 AM	- completed
4572987	0000164914	LIGHTING EMERGENCY 01 AYLNER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	6/1/25 12:00 AM	7/4/25 08:59 AM	7/4/25 08:59 AM	-completed OSHA inspections and signoffs on site
4577120			6643, Aylmer OPC Pump	OPER	Inspection	0		6643-SPAY 6643, Aylmer OPC Pumping Stn	CLOSE	6/1/25 12:00 AM	9/29/25 11:46 AM	9/29/25 11:46 AM	
4586756	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLNER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	6/1/25 12:00 AM	7/4/25 09:01 AM	7/4/25 09:01 AM	-generator ran during power outage. Supplied power to PS, all functioned properly. Paperwork completed by on-call operator.
4589612			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	6/1/25 12:00 AM	7/4/25 09:04 AM	7/4/25 09:04 AM	-alarm testing complete for month of June, alarms received and acknowledged.
4593008			6643, Aylmer OPC Pump	PM	Compliance	1	YEARS	1Y Inspection of Vertical Assets - OPC 6643	CLOSE	6/1/25 12:00 AM	10/16/25 08:03 AM	10/16/25 08:03 AM	-completed
4605349			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	6/9/25 12:00 AM	7/4/25 09:05 AM	7/4/25 09:05 AM	-completed grounds and building clean up and maintenance.
4606060	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLNER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	Engine Diesel Insp/Service (1y) - 6643	CLOSE	6/11/25 12:00 AM	9/5/25 01:50 PM	9/5/25 01:50 PM	-gencare completed inspection August 26
4634901	0000164914	LIGHTING EMERGENCY 01 AYLNER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	7/2/25 12:00 AM	9/16/25 12:14 PM	9/16/25 12:14 PM	
4645985	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLNER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	7/2/25 12:00 AM	8/19/25 02:04 PM	8/19/25 02:04 PM	-completed generator test for 1 hour on load

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4652591			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	7/2/25 12:00 AM	8/19/25 02:05 PM	8/19/25 02:05 PM	-completed alarm testing for the month of july
4660752			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	7/9/25 12:00 AM	7/16/25 09:09 AM	7/16/25 09:09 AM	-completed building and grounds tidying by sweeping
4679270	0000164914	LIGHTING EMERGENCY 01 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	8/1/25 12:00 AM	8/29/25 08:14 AM	8/29/25 08:14 AM	-
4690628	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	8/1/25 12:00 AM	8/12/25 02:23 PM	8/12/25 02:23 PM	-completed
4693145			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	8/1/25 12:00 AM	8/12/25 02:25 PM	8/12/25 02:25 PM	-completed
4708268			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	8/9/25 12:00 AM	8/29/25 08:16 AM	8/29/25 08:16 AM	-completed
4727982	0000164914	LIGHTING EMERGENCY 01 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	9/1/25 12:00 AM	9/12/25 03:04 PM	9/12/25 03:04 PM	-completed
4731463			6643, Aylmer OPC Pump	OPER	Inspection	0		6643-SPAY 6643, Aylmer OPC Pumping Stn	COMP	9/1/25 12:00 AM	11/27/25 09:00 AM	11/27/25 09:00 AM	
4733123			6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Contact Chamber Clean Out Aylmer OPC Pumping Stn (1y) - 6643	BUSCOMP	9/1/25 12:00 AM	12/2/25 02:21 PM	12/2/25 02:21 PM	-completed wet well cleanout with CC Dance, Grease Blanket covered 75% of wet well surface area prior to cleaning. Grease blanket is not longer present and all appears normal.
4733132			6643, Aylmer OPC Pump	OPER	HEALTH AND SAFETY	1	YEARS	OHSA Inspection Aylmer OPC Pumping Stn (1y) - 6643	CLOSE	9/1/25 12:00 AM	9/18/25 02:43 PM	9/18/25 02:43 PM	OHSA Inspection -The OHSA inspection was completed February 26th, 2025 by Rinku Patel. There were no issues identified.
4741119	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	9/1/25 12:00 AM	9/12/25 03:08 PM	9/12/25 03:08 PM	-completed

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4743900			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	9/1/25 12:00 AM	9/12/25 03:10 PM	9/12/25 03:10 PM	-completed
4760673			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	9/9/25 12:00 AM	9/12/25 03:11 PM	9/12/25 03:11 PM	-completed
4780191	0000164914	LIGHTING EMERGENCY 01 AYLME R OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	CLOSE	10/1/25 12:00 AM	10/1/25 02:39 PM	10/1/25 02:39 PM	
4780563	0000164913	FIRE EXTINGUISHER 01 AYLME R OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	YEARS	Fire Extinguisher Inspection Aylmer OPC (1y) - 6643	CLOSE	10/1/25 12:00 AM	10/8/25 08:11 AM	10/8/25 08:11 AM	-completed inspection of unit. Pressure within green section of gauge. Unit accessible to operators.
4795126	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	CLOSE	10/1/25 12:00 AM	10/14/25 02:55 PM	10/14/25 02:55 PM	-OPC pumping station generator test run for 1 hour and completed required paperwork. Transfer switch successful. Generator provides adequate power to pumping station, generator performs well.
4795145	0000164903	PANEL BREAKER MAIN AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Panel Breaker Service (1y) - 6643	COMP	10/1/25 12:00 AM	12/17/25 08:32 AM	12/17/25 08:32 AM	-completed panel breaker inspection. Panel clean and in good working order.
4795147	0000164890	PANEL BREAKER AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Panel Breaker Inspection (1y) - 6643	COMP	10/1/25 12:00 AM	11/21/25 03:29 PM	11/21/25 03:29 PM	-Completed Panel Breaker test during power fail alarm test earlier in the year. Switch operates effectively and no broken components were observed. All in good working order.
4795149	0000164886	PANEL SURGE ARRESTER AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Panel Surge Service (1y) - 6643	COMP	10/1/25 12:00 AM	11/12/25 09:48 AM	11/12/25 09:48 AM	-completed in October. no problems
4795151	0000164892	TRANSMITTER PRESSURE AYLME R OPC PS	6643, Aylmer OPC Pump	PM	Calibration	1	YEARS	Transmitter Pressure (1y) Service (wh) 6643	COMP	10/1/25 12:00 AM	12/17/25 08:34 AM	12/17/25 08:34 AM	-Pressure transmitter accurate and in good working order in accordance with other pressure transmitter - comparable readings. All appears normal.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4795605	0000334551	VALVE KNIFE GATE PUMP DISCH HEADER AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/Replace/Repair	1	YEARS	Valve Gate Inspection/Maintenance (1y) 6643	COMP	10/1/25 12:00 AM	11/21/25 03:31 PM	11/21/25 03:31 PM	-Exercised pump 1 valve gate, was very easy to exercise, no valve stem grease needed. Fully closed and reopened. Tested pumps in hand afterwards to ensure fully open.
4795608	0000334548	VALVE KNIFE GATE PUMP DISCH ISOL AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/Replace/Repair	1	YEARS	Valve Gate Inspection/Maintenance (1y) 6643	COMP	10/1/25 12:00 AM	11/21/25 03:32 PM	11/21/25 03:32 PM	-Exercised pump 2 valve gate, was very easy to exercise, no valve stem grease needed. Fully closed and reopened. Tested pumps in hand afterwards to ensure fully open.
4795611	0000334547	VALVE CHECK 02 PUMP DISCH AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/Replace/Repair	1	YEARS	Valve Check (1y) Inspection (wh) 6643	COMP	10/1/25 12:00 AM	12/18/25 10:37 AM	12/18/25 10:37 AM	-completed check valve inspection with OIC, ensuring proper operation by engaging and disengaging check valve manually.
4795613	0000334546	VALVE CHECK 01 PUMP DISCH AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/Replace/Repair	1	YEARS	Valve Check (1y) Inspection (wh) 6643	COMP	10/1/25 12:00 AM	12/18/25 10:37 AM	12/18/25 10:37 AM	-completed check valve inspection with OIC, ensuring proper operation by engaging and disengaging check valve manually.
4795615	0000334549	VALVE AIR RELEASE HEADER AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/Replace/Repair	1	YEARS	Valve Pressure Relief (1y) (wh) 6643	COMP	10/1/25 12:00 AM	12/18/25 10:48 AM	12/18/25 10:48 AM	-inspection completed and passed
4795627	0000334556	UPS BATTERY BANK PLC PANEL AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	UPS Insp/Service (1y) - 6643	COMP	10/1/25 12:00 AM	11/12/25 09:49 AM	11/12/25 09:49 AM	-completed . UPS in good condition
4798239			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	CLOSE	10/1/25 12:00 AM	10/14/25 02:58 PM	10/14/25 02:58 PM	-completed high level alarm check as well as simulated power fault alarm using generator transfer switch. All alarms received and acknowledged.
4815933			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	CLOSE	10/9/25 12:00 AM	10/22/25 03:41 PM	10/22/25 03:41 PM	-completed cleaning of facility and space surrounding facility. All maintained properly.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4833644	0000164914	LIGHTING EMERGENCY 01 AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	COMP	11/1/25 12:00 AM	11/12/25 03:38 PM	11/12/25 03:38 PM	-Completed OSHA sign offs and ensured all materials are in good working order and fire extinguisher is pressurized (certified last month).
4838202			6643, Aylmer OPC Pump	PM	Compliance	1	YEARS	FEP Review Aylmer OPC Pumping Stn (1y) - 6643	COMP	11/1/25 12:00 AM	12/10/25 08:07 AM	12/10/25 08:07 AM	FEP Review -OPC PS's FEP reviewed.
4838487			6643, Aylmer OPC Pump	PM	Compliance	2	YEARS	FEP Site Plan Review Aylmer OPC (2y) - 6643	COMP	11/1/25 12:00 AM	12/10/25 08:26 AM	12/10/25 08:26 AM	FEP Site Plan Review -OPC PS's FEP site plan reviewed.
4844553	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	COMP	11/1/25 12:00 AM	12/1/25 08:43 AM	12/1/25 08:43 AM	-completed generator run for 1 hour. Fixed ECU alarm problem by topping up the coolant level. All appears normal.
4844572	0000164883	HEATER ELECTRIC 01 HVAC SYS AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	Refurbish/ Replace/Repair	1	YEARS	Heater Electric (1y) Inspection 6643	COMP	11/1/25 12:00 AM	12/2/25 02:28 PM	12/2/25 02:28 PM	-inspected heater and ensured functioning as designed. No blockages detected or dust build-up. Heating spaces adequately and according to thermostat on the wall.
4844577	0000164891	PANEL DISTRIBUTION OPC-SPS AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Panel Breaker 1 Inspection (1y) - 6643	COMP	11/1/25 12:00 AM	11/21/25 03:34 PM	11/21/25 03:34 PM	-Operated breaker and power turned off and returned once breaker flipped back on. All working as intended.
4845014	0000164910	FILTER ELECTRIC HARMONIC 02 RAW SEWAGE PUMP AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Filter Electric Harmonic Service (1y) 6643	COMP	11/1/25 12:00 AM	12/17/25 08:22 AM	12/17/25 08:22 AM	-completed cleaning of filter box. connections clean and sturdy, system running properly. All appears in good working order.
4845016			6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Filter Electric Harmonic Service (1y) 6643	BUSCOMP	11/1/25 12:00 AM	12/17/25 08:23 AM	12/17/25 08:23 AM	-completed cleaning of filter box. connections clean and sturdy, system running properly. All appears in good working order.
4845036	0000164897	FILTER ELECTRIC HARMONIC 01 RAW SEWAGE PUMP AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Filter Electric Harmonic Service (1y) 6643	COMP	11/1/25 12:00 AM	12/17/25 08:23 AM	12/17/25 08:23 AM	-completed cleaning of filter box. connections clean and sturdy, system running properly. All appears in good working order.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4845038	0000164898	FILTER ELECTRIC HARMONIC 02 RAW SEWAGE PUMP OUTPUT AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	YEARS	Filter Electric Harmonic Service (1y) 6643	COMP	11/1/25 12:00 AM	12/17/25 08:24 AM	12/17/25 08:24 AM	-completed cleaning of filter box. connections clean and sturdy, system running properly. All appears in good working order.
4846892			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	COMP	11/1/25 12:00 AM	12/9/25 03:53 PM	12/9/25 03:53 PM	-Completed alarm testing of power fail and high level alarm
4861801			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	COMP	11/9/25 12:00 AM	12/1/25 09:43 AM	12/1/25 09:43 AM	-completed
4862675			Aylmer - OPC Pumping Station	CORR	Refurbish/ Replace/Repair	0		OPC Generator Lockout	COMP		12/18/25 10:49 AM	12/18/25 10:49 AM	- Recieved another generator lockout / fault alarm. Generator not in auto. Acknowledged alarm on SCADA and ensured utility power was still active. Will head there soon to take generator out of lockout and back in auto. Contacted GenTech to book service appointment regarding alarm. Technician stated problem may be battery / charger is faulty and ECU is overriding system, taking it out of auto. GenTech will contact for service appointment to troubleshoot problem next week. 1308: arrived onsite and started up generator to hopefully charge battery until service appointment. Generator paperwork filled out and monitoring charge level. Battery level at 28.5 V and Charger at 27.0 V
4879444	0000164914	LIGHTING EMERGENCY 01 AYLMER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	BUSCOMP	12/1/25 12:00 AM	12/15/25 03:21 PM	12/15/25 03:21 PM	-completed OSHA sign off, all materials within expiry.
4889745	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	COMP	12/1/25 12:00 AM	12/17/25 08:17 AM	12/17/25 08:17 AM	-completed engine generator run for 0.5 hours. transfer successful and all appears normal, no other alarms came out afterwards.

Workorder Summary Report

 Report Start Date: Jan 1, 2025 12:00 AM
 Report End Date: Dec 31, 2025 11:59 PM
 Location: 6643,6643-SPAY
 Work Order Type: CORR,OPER,PM
 Work Order Class:

				WorkOrder		PM Schedule		Workorder Details					
WO #	Asset ID	Asset Description	Location Description	Type	Class	FEQ	Units	Work Order Description	Status	Schedule Start	Actual Start	Actual Finsh	WorkLog Detail
4892057			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	COMP	12/1/25 12:00 AM	12/17/25 08:11 AM	12/17/25 08:11 AM	-completed high level alarm testing and generator run alarms. All alarms received and acknowledged.
4907544			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Building & Grounds Maintenance (1m) - 6643	COMP	12/9/25 12:00 AM	12/17/25 08:10 AM	12/17/25 08:10 AM	-completed grounds and building maintenance.
4929163	0000164914	LIGHTING EMERGENCY 01 AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	HEALTH AND SAFETY	1	MONTHS	OHSA Inspection Aylmer OPC PS (1m) - 6643	COMP	1/1/26 12:00 AM	1/6/26 03:27 PM	1/6/26 03:27 PM	- Completed OSHA material sign off onsite (eyewash, first aid, and fire extinguishers)
4944462	0000164919	GENERATOR W/ DIESEL ENGINE STANDBY AYLMEER OPC PS	6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Engine Diesel Test/Insp (1m) - 6643	COMP	1/1/26 12:00 AM	1/6/26 03:30 PM	1/6/26 03:30 PM	- Completed generator run test for the month. Transfer successful and ran on load.
4947875			6643, Aylmer OPC Pump	PM	Inspection	1	MONTHS	Critical Alarm/Dialer Testing (1m) 6643	COMP	1/1/26 12:00 AM	1/6/26 03:31 PM	1/6/26 03:31 PM	- Completed alarm testing for facility - power failure and high level wet well. Also received alarm for generator transfer. Alarms ack
